GPD1, 47U, 800 x 1000mm

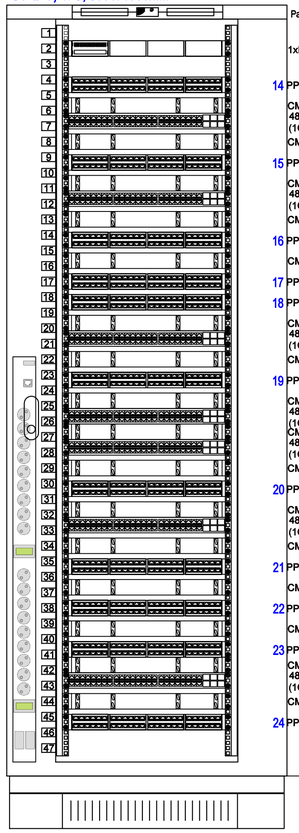

Panel wentylacyjny 4-wentylatorowy

1xFiberModHD-sp-6lcd-z-pc-c-os2-bk, FO12J do GPD2

14 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel
48 RJ-45 10/100/1G BaseT PoE+, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 920W AC supply, 2xSFP-10G-SR
CM 1U 19" Metal Panel

15 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel
48 RJ-45 10/100/1G BaseT PoE+, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 920W AC supply, 2xSFP-10G-SR
CM 1U 19" Metal Panel

16 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

17 PP HD, 1U-48xRJ45-C6A, S/FTP

18 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel
48 RJ-45 10/100/1G BaseT PoE+, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 920W AC supply, 2xSFP-10G-SR
CM 1U 19" Metal Panel

19 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel
48 RJ-45 10/100/1G BaseT PoE+, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 920W AC supply, 2xSFP-10G-SR
CM 1U 19" Metal Panel
48 RJ-45 10/100/1G BaseT PoE+, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 920W AC supply, 2xSFP-10G-SR
CM 1U 19" Metal Panel

20 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel
48 RJ-45 10/100/1G BaseT PoE+, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 920W AC supply, 2xSFP-10G-SR
CM 1U 19" Metal Panel

21 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

22 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

23 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel
48 RJ-45 10/100/1G BaseT PoE+, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 920W AC supply, 2xSFP-10G-SR
CM 1U 19" Metal Panel

24 PP HD, 1U-48xRJ45-C6A, S/FTP

Listwa zasilająca z monitoringiem przez Eth IP, I-fazowa, 32A, 18 Gniazd z uziemieniem, montaż z tyłu szafy, zasilanie z TSR/3.4

Listwa zasilająca z monitoringiem przez Eth IP, I-fazowa, 32A, 18 Gniazd z uziemieniem, montaż z tyłu szafy, zasilanie z TSR/3.3

GND < 10Ω

GPD2, 47U, 800 x 1000mm

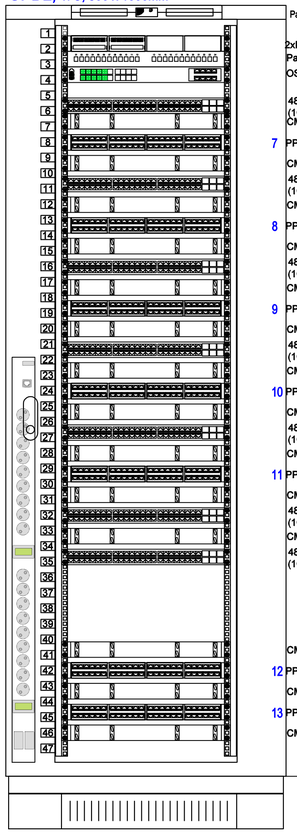

Panel wentylacyjny 4-wentylatorowy

2xFiberModHD-sp-6lcd-z-pc-c-os2-bk, 4 x FO 12J (z GPD 1,3)
Panel światłowodowy 24x duplex
OS-X20, 20x10G SFP+ Ports, 8xGbE, przełącznik agregujący

48 RJ-45 10/100/1G BaseT PoE+, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 920W AC supply, 2xSFP-10G-SR
CM 1U 19" Metal Panel

7 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

48 RJ-45 10/100/1G BaseT, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 150W AC supply
CM 1U 19" Metal Panel

8 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

48 RJ-45 10/100/1G BaseT, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 150W AC supply
CM 1U 19" Metal Panel

9 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

48 RJ-45 10/100/1G BaseT, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 150W AC supply
CM 1U 19" Metal Panel

10 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

48 RJ-45 10/100/1G BaseT, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 150W AC supply
CM 1U 19" Metal Panel

11 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

48 RJ-45 10/100/1G BaseT PoE+, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 920W AC supply, 2xSFP-10G-SR
CM 1U 19" Metal Panel

48 RJ-45 10/100/1G BaseT, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 150W AC supply

CM 1U 19" Metal Panel

12 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

13 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

Listwa zasilająca z monitoringiem przez Eth IP, I-fazowa, 32A, 18 Gniazd z uziemieniem, montaż z tyłu szafy, zasilanie z TSR/3.2

GND < 10Ω

GPD3, 47U, 800 x 1000mm

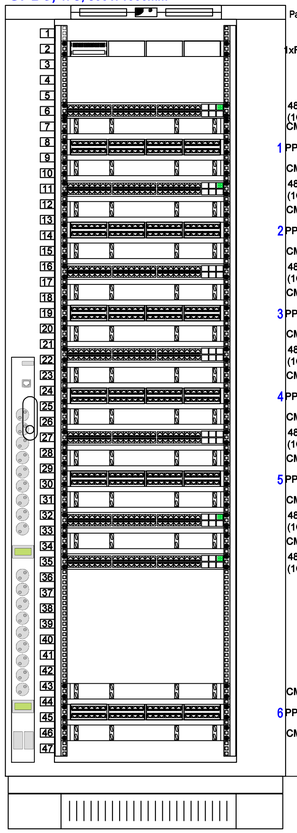

Panel wentylacyjny 4-wentylatorowy

1xFiberModHD-sp-6lcd-z-pc-c-os2-bk, FO12J do GPD2

48 RJ-45 10/100/1G BaseT PoE+, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 920W AC supply, 2xSFP-10G-SR
CM 1U 19" Metal Panel

1 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

48 RJ-45 10/100/1G BaseT, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 150W AC supply
CM 1U 19" Metal Panel

2 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

48 RJ-45 10/100/1G BaseT, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 150W AC supply
CM 1U 19" Metal Panel

3 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

48 RJ-45 10/100/1G BaseT, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 150W AC supply
CM 1U 19" Metal Panel

4 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

48 RJ-45 10/100/1G BaseT, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 150W AC supply
CM 1U 19" Metal Panel

5 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

48 RJ-45 10/100/1G BaseT PoE+, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 920W AC supply, 2xSFP-10G-SR
CM 1U 19" Metal Panel

48 RJ-45 10/100/1G BaseT, 2xSFP(1G) and 4xSFP+
(1G/10G) uplink/stacking ports, 150W AC supply

CM 1U 19" Metal Panel

6 PP HD, 1U-48xRJ45-C6A, S/FTP

CM 1U 19" Metal Panel

GND < 10Ω

INWESTOR	**Izba Administracji Skarbowej w Olsztynie** Al. Marszałka Józefa Piłsudzkiego 59A, 10-950 Olsztyn
JEDNOSTKA PROJEKTUJĄCA	**POWERSUN Sp. z o.o.** ul. Diamentowa 2 20-447 Lublin
NAZWA PROJEKTU	Modernizacja sieci komputerowej LAN Izby Administracji Skarbowej w Olsztynie w budynku Urzędu Skarbowego w Olsztynie przy al. Marszałka Józefa Piłsudskiego 59
STADIUM PROJEKTU	**DOKUMENTACJA POWYKONAWCZA**
BRANŻA	TELETECHNICZNA / ELEKTRYCZNA
OBIEKT	Urząd Skarbowy w Olsztynie al. Marszałka Józefa Piłsudskiego 59, 10-950 Olsztyn Nr ew. dz.: 21/2, jedn. ewid.: 286201_1, obręb Olsztyn 74
TEMAT RYSUNKU	**Widoki szaf GPD1 - GPD3**

			PODPIS
OPRACOWAŁ	mgr Dariusz Rybaczyk	WAM/0052/ ZHOT/05	
Specjalność	telekomunikacyjna		

DATA	NR RYSUNKU	REWIZJA	SKALA
12.2021	E-16	A	---
